



Construction Update

Construction activity continues within the Randwick Campus Redevelopment site, which incorporates the Prince of Wales Hospital Acute Services Building (ASB) and associated UNSW Eastern Extension, along with the future Sydney Children's Hospital Stage 1 and Minderoo Children's Comprehensive Cancer Centre (SCH1/MCCCC) building, and UNSW's Health Translation Hub (HTH).

Upcoming activities

Sydney Children's Hospital Stage 1 and Minderoo Children's Comprehensive Cancer Centre

Structural works continue to progress for the SCH1/MCCCC building, with final stages of detailed excavation and inground services now finalised. Basement level concrete slabs are complete and suspended slabs are under construction, alongside lift shafts and stairwells for the 12-storey building.

To support ongoing activities, protective screens are being installed around the construction zone and will continue to be erected during September.

Night works are scheduled to occur in September (weather permitting) to install a protective overhead gantry hoarding at the corner of High Street and Hospital Road, which may result in intermittent construction noise. Detailed information will be

provided to nearby stakeholders ahead of activities commencing.

Intermittent out of hours activities to deliver construction materials and equipment are also planned during September.

Prince of Wales Hospital Acute Services Building and UNSW Eastern Extension

Alongside ongoing works within the new ASB to deliver additional inpatient units, internal fit-out activities for the UNSW Eastern Extension will also continue throughout September.

Additional activities within the UNSW Eastern Extension include partitioning and service installation works for drainage and fire systems.

Weekend activities to install glazing on the western façade of the ASB building are planned for early September. Detailed information will be provided to affected stakeholders ahead of works commencing.

UNSW Health Translation Hub


Piling and bulk excavation continues within the UNSW HTH site in readiness for detailed excavation.

To support this, early hours activity to deliver construction machinery and equipment will occur throughout September.

Weekend site activity is also planned for early September (weather permitting) to install a second tower crane to support ongoing construction of the UNSW HTH.

A weekend road closure will again be required to enable delivery of the tower crane via the Botany Street construction site access gate. Detailed information will be provided to nearby stakeholders ahead of works commencing.

Map of construction activities September 2023

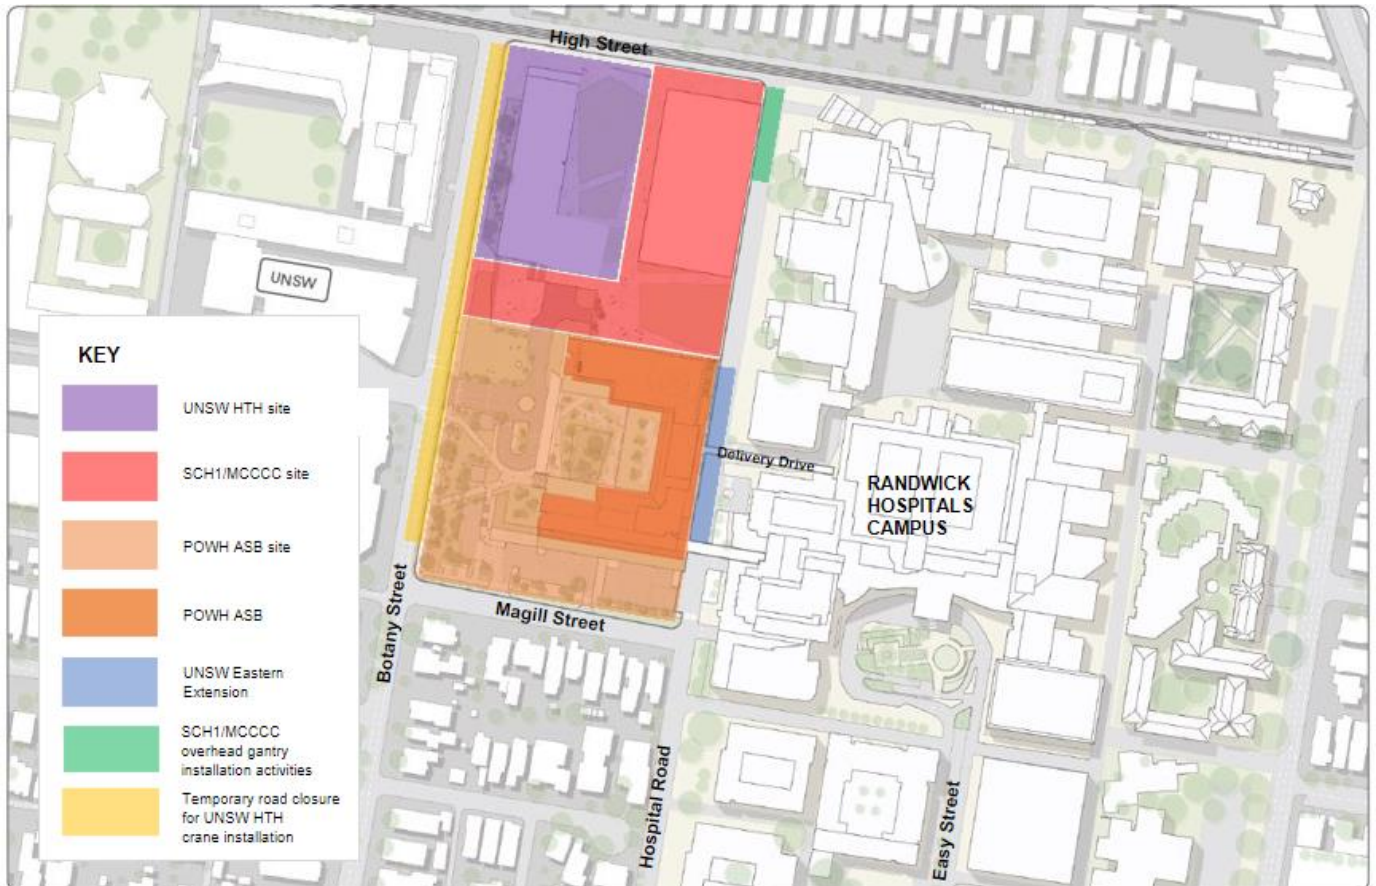

Managing construction activities

We are committed to minimising the impact of our works. All construction activities are carried out with the health and safety of the local community and site workers as our top priority.

We endeavour to keep noise, dust and vibration to a minimum.

Where possible, activities are scheduled during approved site hours of **Monday to Friday, 7am to 6pm and Saturday, 8am to 5pm**. Work may be delayed or rescheduled due to weather or unforeseen circumstances such as workforce availability.

Out of hours work will continue to be communicated directly to affected stakeholders. All activity dates and times are subject to change.

Please note that service upgrades unrelated to the redevelopment project may also be undertaken by other agencies at any given time without notification.



View our [interactive map](#) for the latest information on construction activities across campus, or to learn more about each of the Randwick Campus Redevelopment projects.
