



Construction Update

There's been significant progress on the Randwick Campus Redevelopment site throughout 2023, with main works well underway on both the Sydney Children's Hospital Stage 1 and Minderoo Children's Comprehensive Cancer Centre (SCH1/MCCCC) building and UNSW's Health Translation Hub (HTH), alongside ongoing internal fit-out activities within the Prince of Wales Hospital Acute Services Building (ASB) and associated UNSW Eastern Extension.

Learn more about how these exciting projects will shape future healthcare by visiting our website at randwickcampusredevelopment.health.nsw.gov.au

Upcoming activities

Sydney Children's Hospital Stage 1 and Minderoo Children's Comprehensive Cancer Centre

Suspended slab pours have been completed to Level 5, with construction of core structural components including elevator shafts and stairwells progressed to Level 8.

Construction of the walls and service rough-ins have commenced within the lower levels of the new building, including the future loading dock and Emergency Department, with formwork stripping underway up to Level 3.

Weekend crane activity is planned in December along with out of hours delivery of construction materials and equipment. Information will be communicated to affected stakeholders ahead of the of these activities.

Essential electricity supply works under an Ausgrid authority approval will be undertaken early in the new year, requiring some pedestrian and vehicle

diversions on High Street and Botany Street in the vicinity of the construction site and up to three evenings of night works.

Holiday period site closures

Following a busy year of construction, our project sites will close for the holiday period:

SCH1/MCCCC – closed from 6pm on Friday 22 December, reopening from 7am on Monday 8 January 2024.

HTH – closed from 6pm on Friday 22 December, reopening from 7am on Wednesday 3 January 2024.

Internal fit-out works within the POWH ASB will also pause from 23 December to 7 January.

Please note that minor internal fit-out works within the UNSW Eastern Extension will continue throughout the closure period during normal construction hours.

Prince of Wales Hospital Acute Services Building

Hospital operational commissioning activities have commenced in the additional inpatient units and Education, Training and Research space on Level 6 of the ASB. This includes the installation of furniture, equipment and stock; training and orientation for clinical and non-clinical staff; and clinical cleans.

Internal fit-out works are scheduled to begin in the new year for the additional operating theatres on Level 1, alongside refurbishment activities within vacated departments on the existing campus.

UNSW Eastern Extension


Internal fit-out across the 10 floors of the future

research and learning spaces continues. Throughout December, ceiling framing, painting and floor finishing installation will be underway to prepare the spaces for operational use in 2024.

UNSW Health Translation Hub

Construction activities continue, including bulk excavation and concrete pours planned in December. Upcoming works to support construction of the link bridge connecting the existing university campus to the new building will include regular Saturday activity and impact pedestrian routes on Botany Street. Detailed information will be provided to affected stakeholders ahead of activities commencing.

Map of construction sites – December 2023

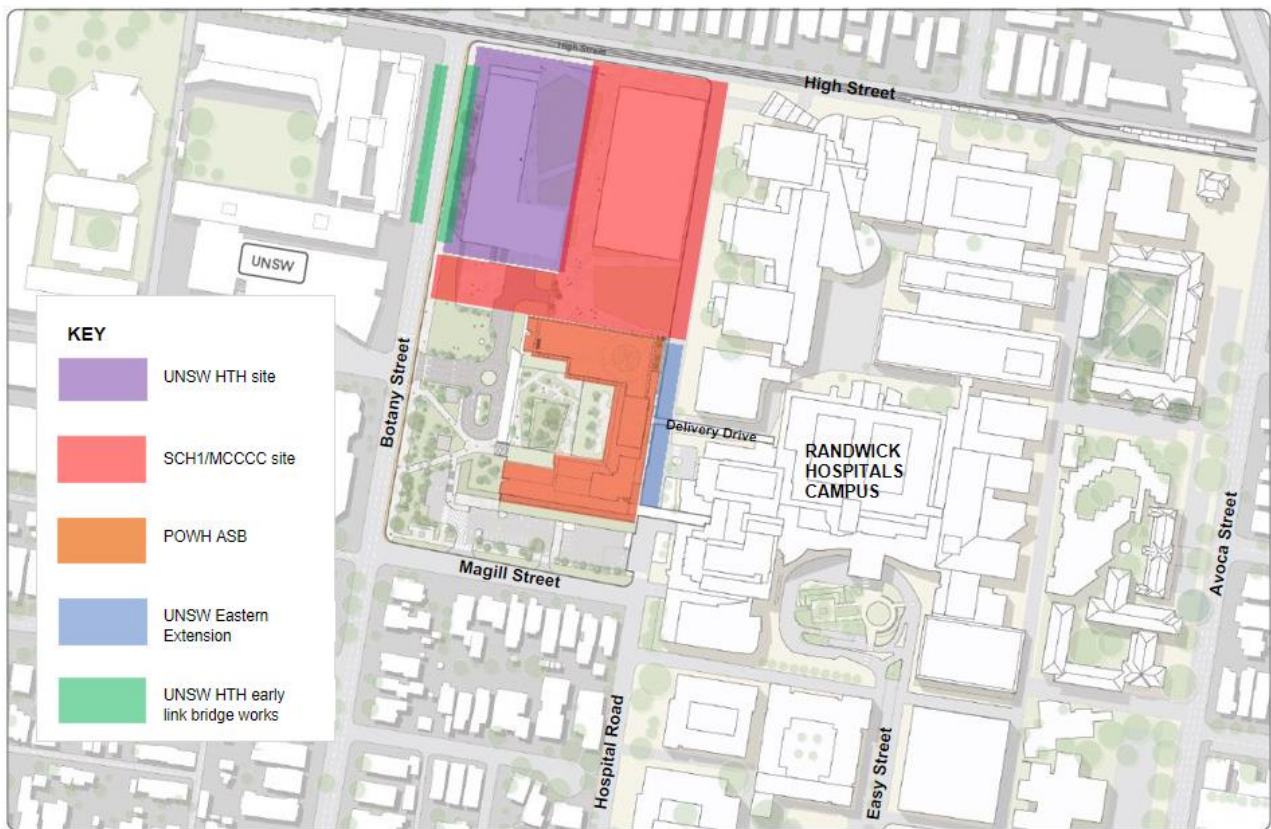

Managing construction activities

We are committed to minimising the impact of our works. All construction activities are carried out with the health and safety of the local community and site workers as our top priority.

We endeavour to keep noise, dust and vibration to a minimum.

Where possible, activities are scheduled during approved site hours of **Monday to Friday, 7am to 6pm and Saturday, 8am to 5pm**. Work may be delayed or rescheduled due to weather or unforeseen circumstances such as workforce availability.

Please note that service upgrades unrelated to the redevelopment project may also be undertaken by other agencies at any given time without notification.

Out of hours work will continue to be communicated directly to affected stakeholders. All activity dates and times are subject to change.

View our [interactive map](#) for the latest information on construction activities, or to learn more about each of the **Randwick Campus Redevelopment projects.**

