

Construction Update

The NSW Government is investing more than \$1 billion in the Randwick Health & Innovation Precinct, strengthening health, research, education and innovation outcomes to ensure NSW is at the forefront of health research and education internationally.

The Prince of Wales Hospital Acute Services Building main works are nearing completion, and construction on the Sydney Children's Hospital Stage 1 and Minderoo Children's Comprehensive Cancer Centre is underway.

Activities in September 2022

Prince of Wales Hospital Acute Services Building construction

Final finishes installation and validation testing continues for all floors of the Acute Services Building. Landscaping at the main entry forecourt and the Emergency Department entry adjacent to Magill Street continues.

Works for the clinical link bridge, the public link bridge and the UNSW Eastern Extension structure will continue in September. Additional information about localised activities will be provided to affected stakeholders.

Activities for the staff End of Trip Facility on level B3 of the campus carpark continue throughout September within a secure construction zone near the vehicle exit.

Sydney Children's Hospital Stage 1 and Minderoo Children's Comprehensive Cancer Centre construction

Early and Enabling Works for the Sydney Children's Hospital Stage 1 and Minderoo Children's Comprehensive Cancer Centre (SCH1/MCCCC) in the northern portion of the site and Hospital Road north is scheduled for completion in mid-September. Final activities include installation of new electrical infrastructure under Hospital Road and the High Street footpath works.

Following completion of Early and Enabling Works, the SCH1/MCCCC Main Works Contractor, John Holland Pty Ltd, is set to begin on site from mid-September. Initial activities will include changes to the hoarding on Hospital Road north.



Botany Street activities

Construction has begun for a new signalised intersection on Botany Street to provide safe pedestrian and vehicle access to the new Prince of Wales Hospital Acute Services Building, future Sydney Children's Hospital Stage 1 and Minderoo Children's Comprehensive Cancer Centre, UNSW Health Translation Hub and UNSW Kensington Campus.

Construction is expected to take approximately four months to complete, subject to weather and unforeseen circumstances. Pedestrian and footpath access will be managed through appropriate diversions. Signage and/or traffic control will be in place to assist, where required.

Works will be undertaken in line with the approved hours provided by TfNSW and Department of Planning and Environment (DPE), including the provision of required respite periods.

For traffic and safety reasons and due to the proximity to the Randwick Health Campus and University, night works are required to safely undertake the works.

Essential gas infrastructure upgrades on Botany Street will be carried out **between Sunday 28 August to Sunday 18 September**. These works are separate to the Randwick Campus Redevelopment and will be undertaken on behalf of Zinfra Gas as night works. Throughout this period, Randwick Campus Redevelopment will not be conducting night works.

Magill Street upgrade

Landscaping activities on Magill Street will continue in September. This work will occur in localised work zones and Magill Street remains accessible to residents throughout the works.

Sewer works have begun and will continue into early September. Magill Street will be closed to traffic for the duration of these works, with resident access maintained from the Hospital Road end only.

Upcoming out of hours work

Hospital Road and Delivery Drive activities

Resurfacing of Hospital Road between Delivery Drive and Barker Street to improve the road surface and line marking will occur at night in September.

Ambulance access will be maintained through Barker Street via Avoca Street to Nurses Drive. Detailed information will be provided to affected stakeholders ahead of the works commencing.

Essential night works for electrical service investigations, installing electrical utilities and driveway works in the Hospital Road north area, adjacent to the Sydney Children's Hospital, will

continue in September. Detailed information will be provided to affected stakeholders.

Managing construction activities

We are committed to minimising the impact of our works where we can.


All construction activities are carried out with the health and safety of the local community as our top priority. We endeavour to keep noise, dust and vibration to a minimum.

Where possible, activities are scheduled during approved site hours **Monday to Friday, 7am to 6pm and Saturday, 8am to 5pm.**

Work may be rescheduled due to weather or unforeseen circumstances such as workforce availability. Any out of hours work will continue to be communicated in advance directly to affected stakeholders.

Thank you for your patience while we progress this important work.

Map of construction activities September 2022

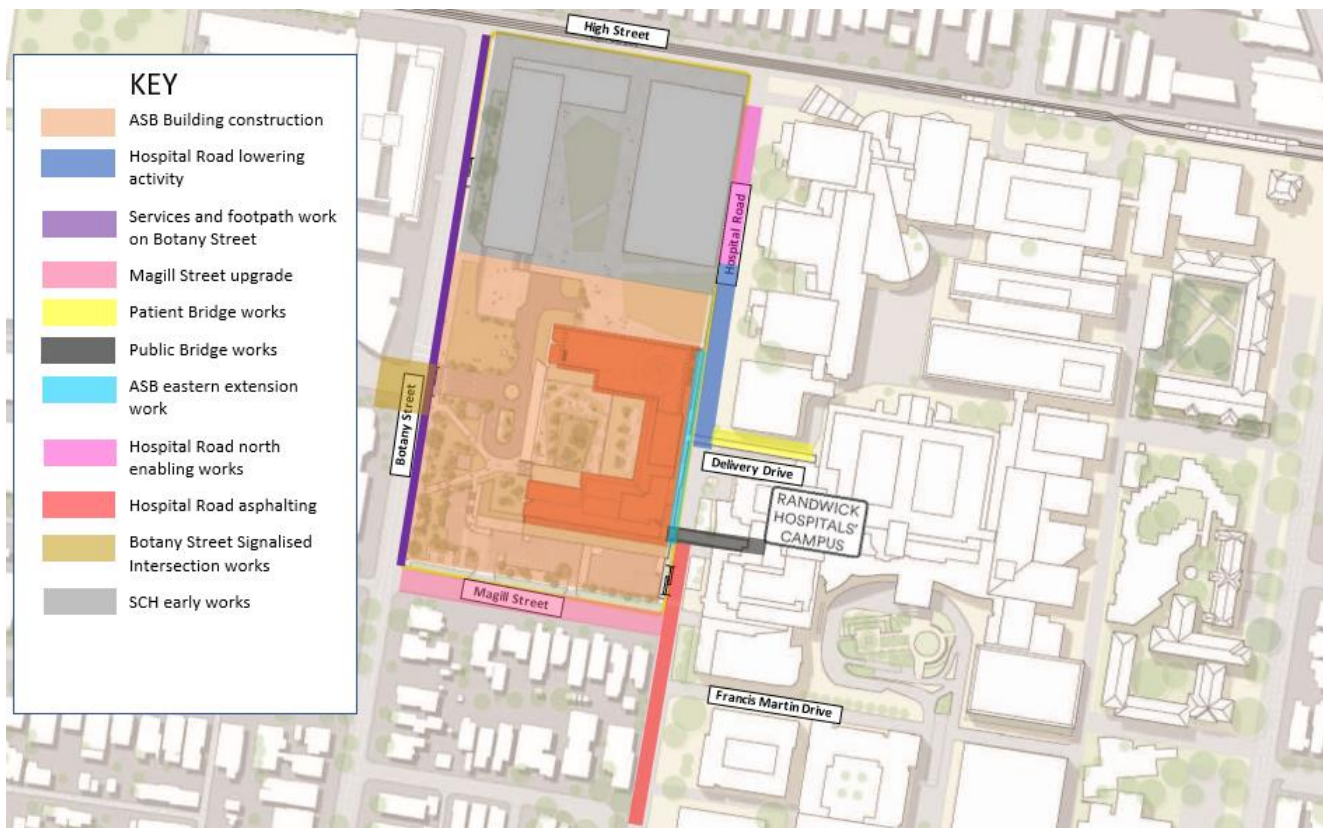

1800 571 866



randwickcampusdevelopment@health.nsw.gov.au



randwickcampusredevelopment.nsw.gov.au
